INSPIRE AI

STAND-UP

Standup Meeting



© 2026 Inspire | Confidential

Share one event and choose one next action

Objective · what happened	Describe one event or result from the previous training day.
Reflective · how you felt	Name a feeling. Share only what you choose to share.
Interpretive · what it means	Explain the learning you take from that event.
Decisional · what next	State one action you will take into the rest of the day.

© 2026 Inspire | Confidential

INSPIRE AI

REVIEW

Review the Revised MVP

Overnight cut, peer inspection



© 2026 Inspire | Confidential

PRACTICE

Write User Stories for the MVP

Practice only — do not reopen discovery



© 2026 Inspire | Confidential

Story · INVEST · Acceptance Criteria

User story

As a <stakeholder>

I want <capability>

So that <outcome>

INVEST

Independent

Negotiable

Valuable

Estimable

Sized appropriately

Testable


AC · G/W/T

Given context

When action


Then observable result

Happy · sad · exception

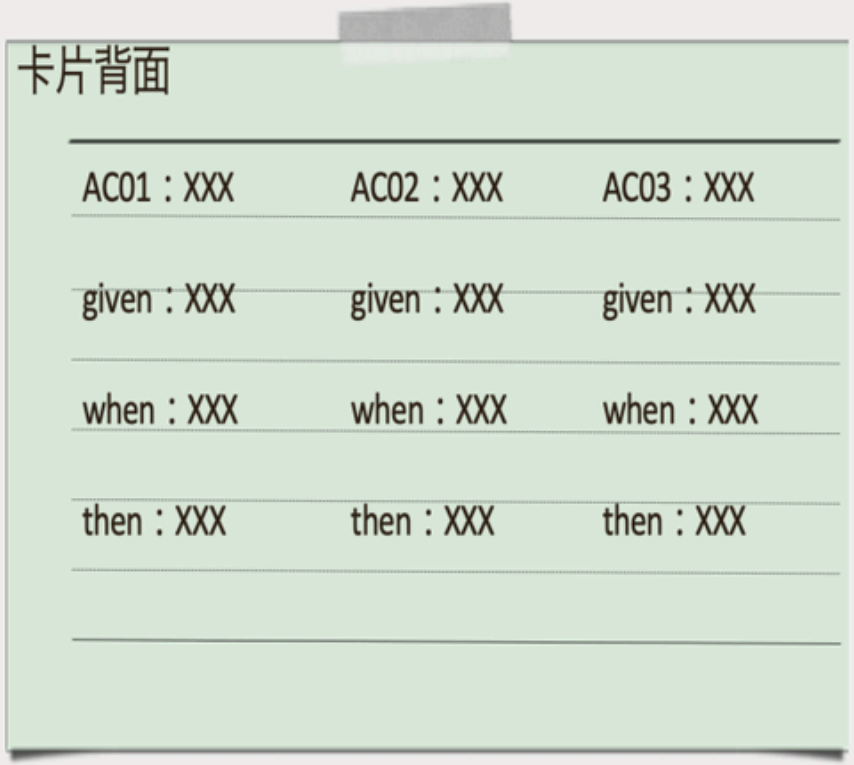

© 2026 Inspire | Confidential


Product Backlog

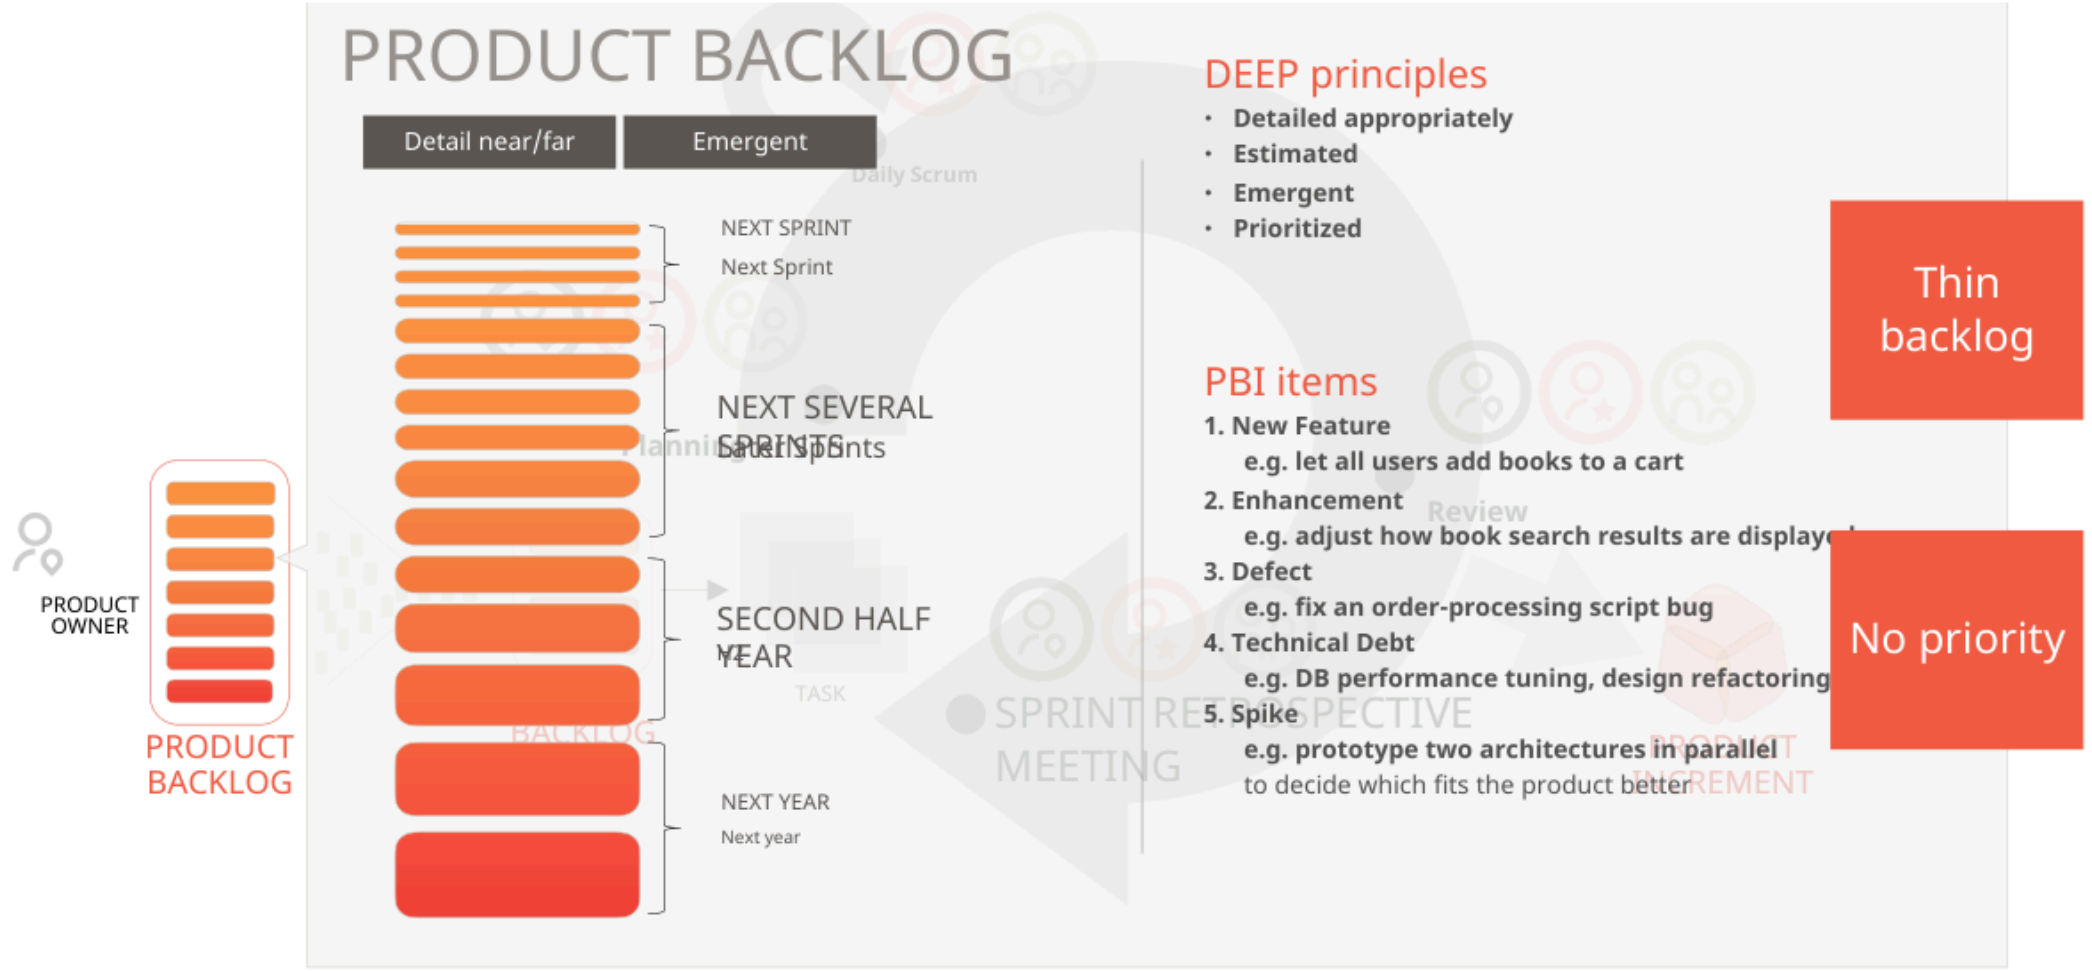

© 2026 Inspire | Confidential

MoSCoW prioritization

Must Have **Highest priority**	
Should Have **Desirable to have**	Ship still happens, but value and UX suffer sharply
Could Have **Nice to have**	Nice to have — limited impact if missed
Won’t Have **Out of scope**	

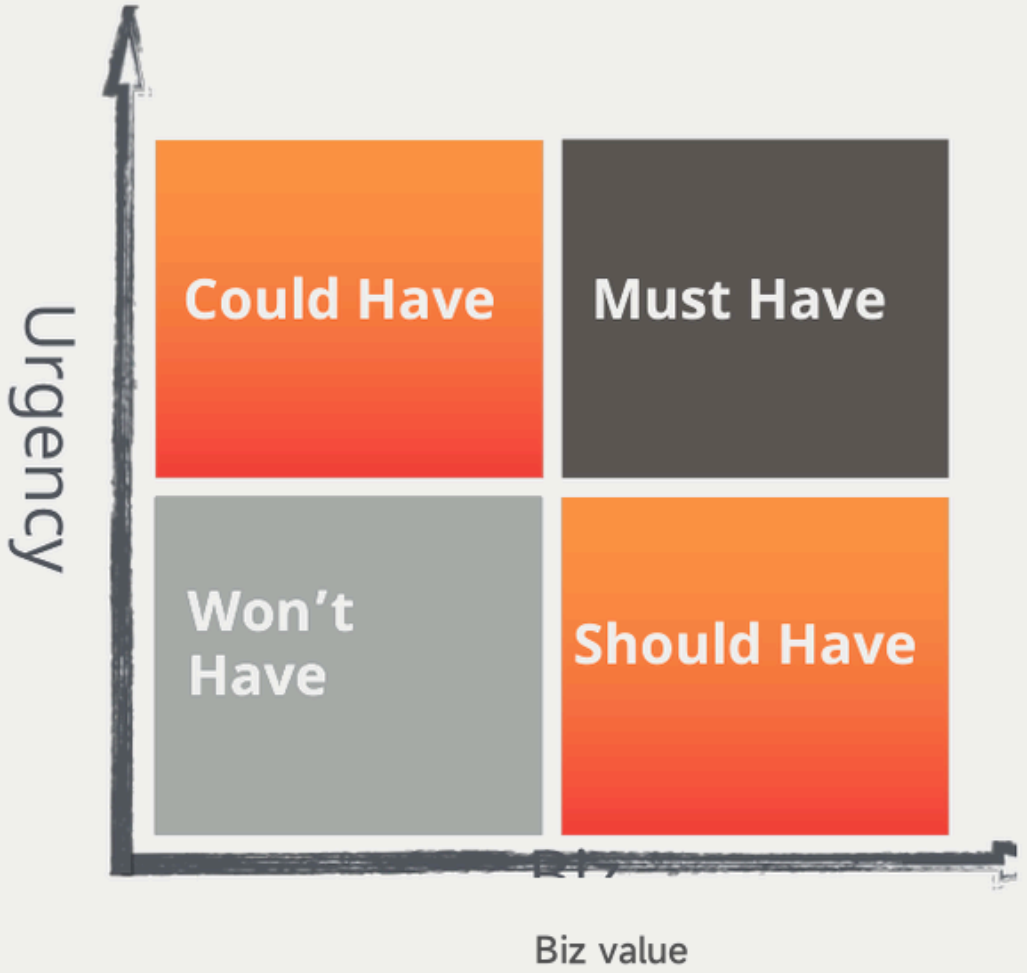

© 2026 Inspire | Confidential

BREAK

Take a short break



© 2026 Inspire | Confidential

INSPIRE AI

SHOWCASE

MVP User Story Showcase

Inspect stories, not a final demo



© 2026 Inspire | Confidential

Write User Stories for the MVP



BA leads. Team challenges examples.

Only thin, testable stories for the MVP already cut on Day 14.

Do not re-open discovery or invent a new MVP.

Prepare cards for the MVP User Story Showcase.

© 2026 Inspire | Confidential

BREAK

Take a short break



© 2026 Inspire | Confidential

INSPIRE AI

LECTURE

Scrum Essentials and Timeline Detail


Empiricism and the project rhythm · Parts 1–2



© 2026 Inspire | Confidential


What is Scrum

Per the Scrum Guide: Scrum is a framework within which people can address complex adaptive problems, while productively and creatively delivering products of the highest possible value. It is founded on values, principles, and practices.

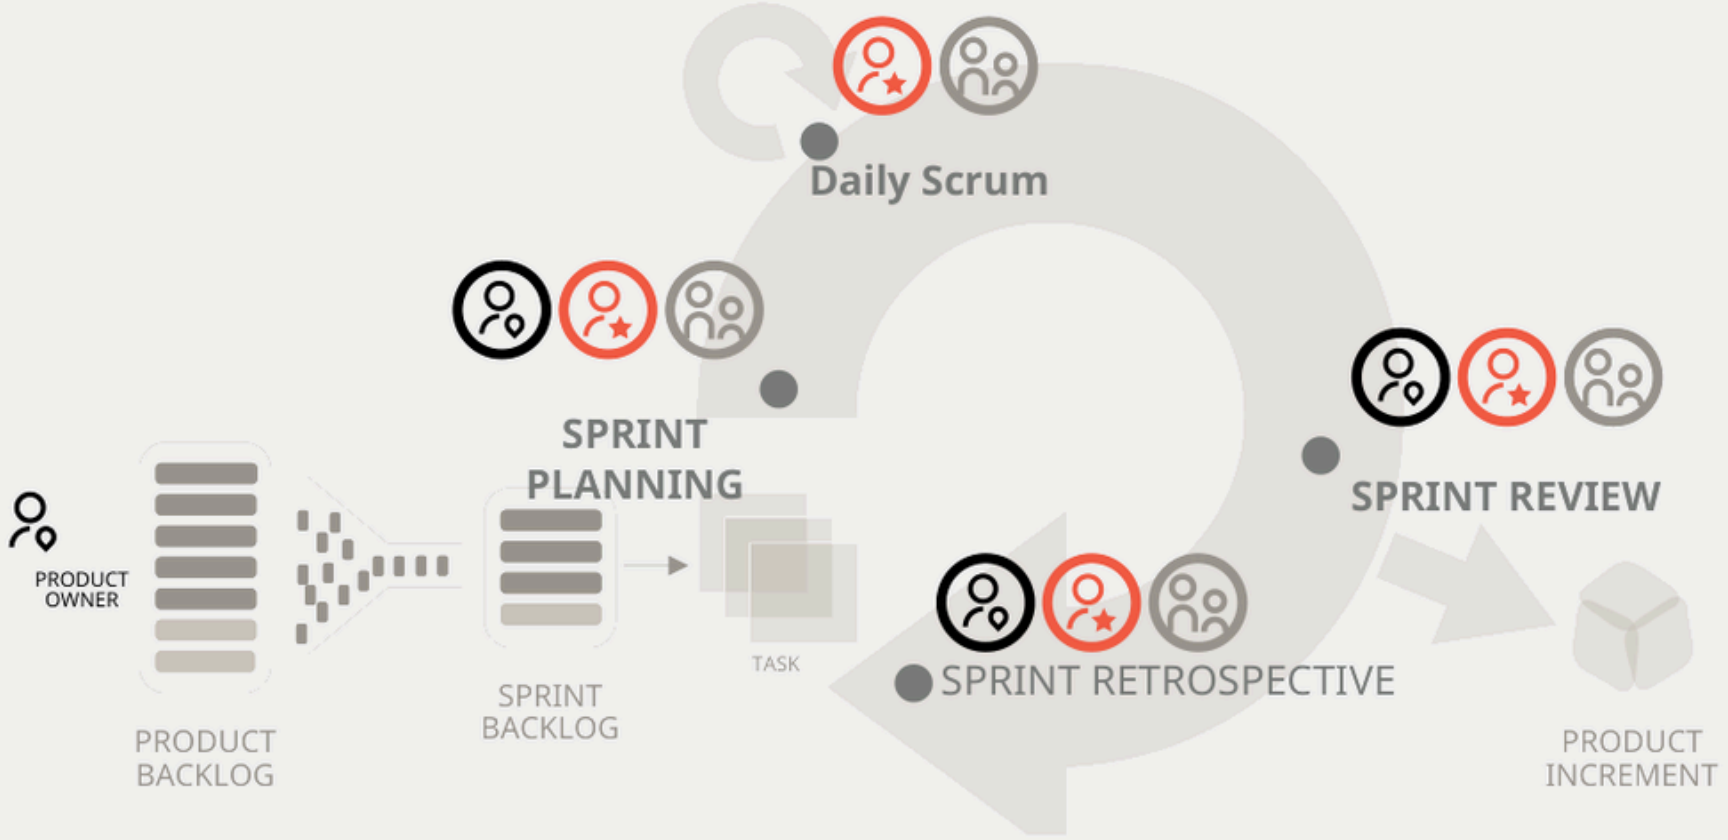

© 2026 Inspire | Confidential

Scrum Overview

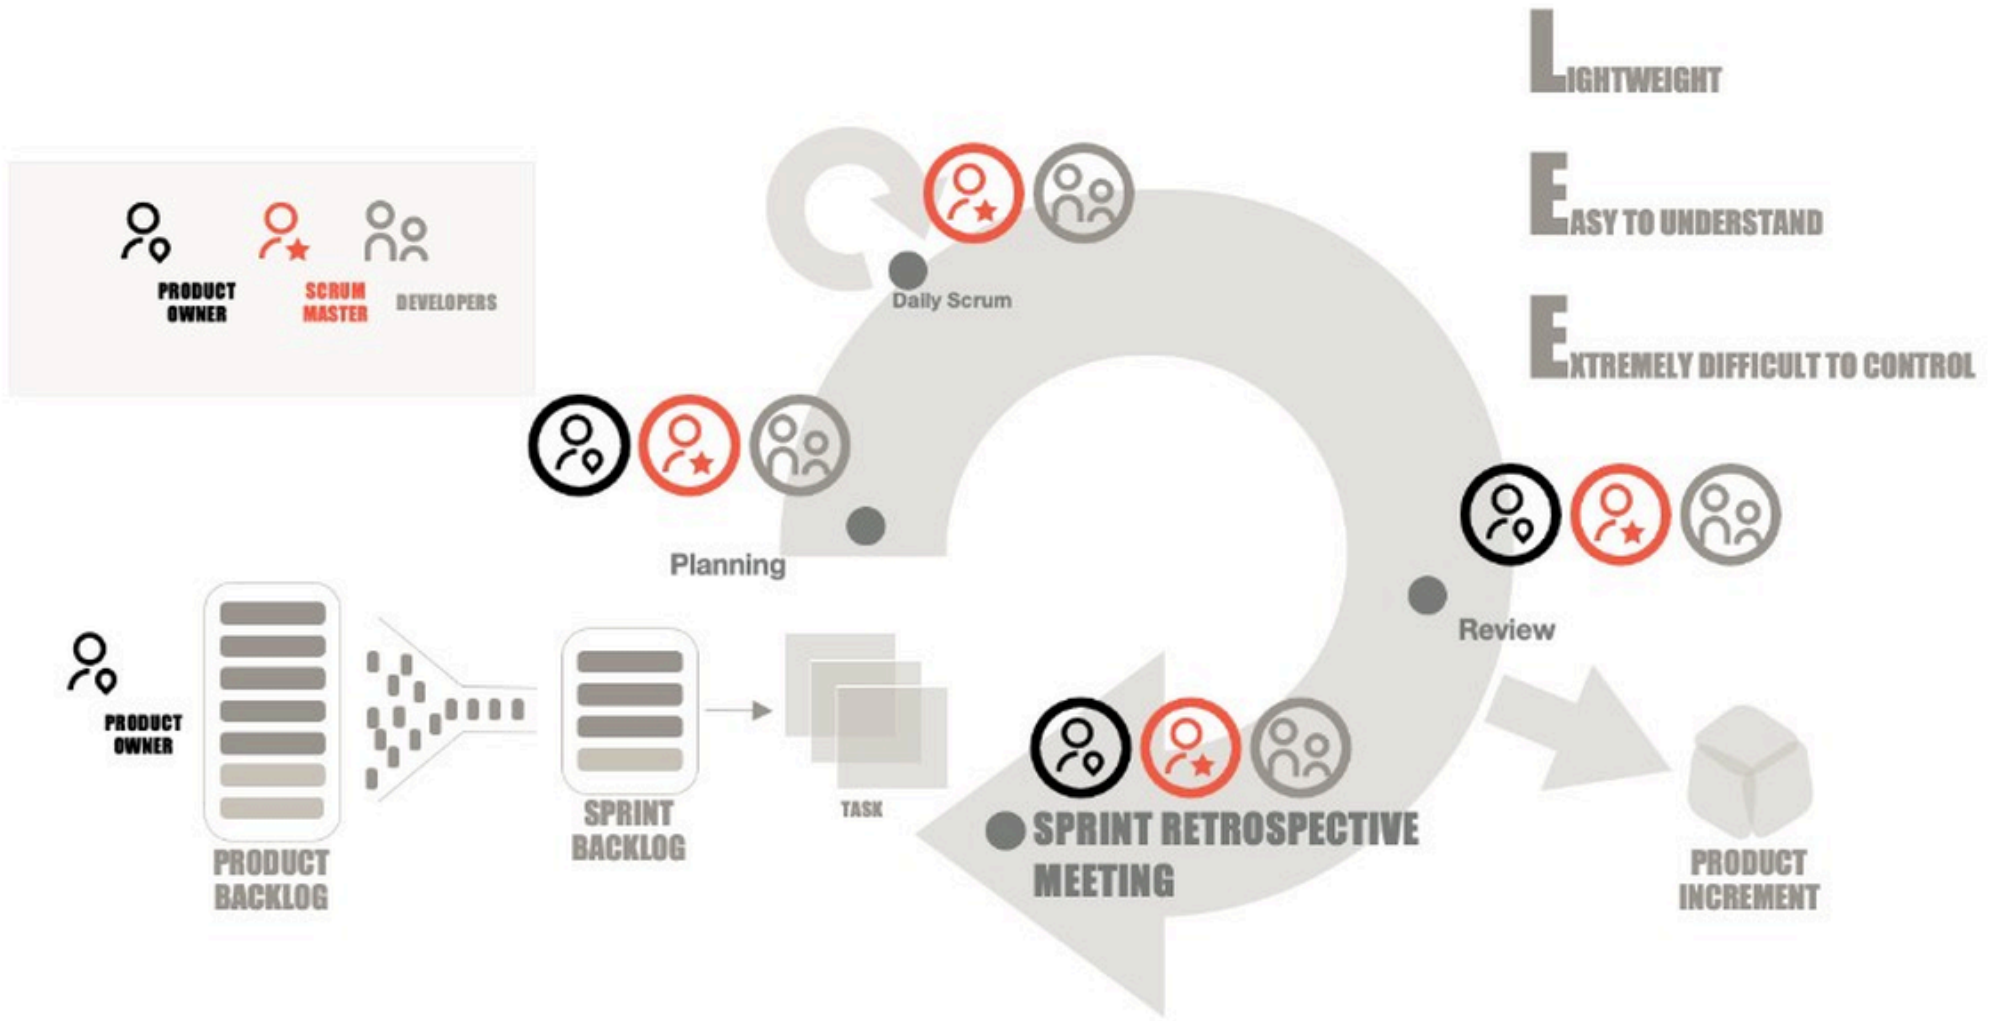

© 2026 Inspire | Confidential

Scrum Framework



- Product Owner: PO — maximizes product value
- Scrum Master: SM — true leader who serves
- Developers: create the usable Increment

- Product Backlog
- Sprint Backlog
- Product Increment

- Focus
- Courage
- Openness
- Commitment
- Respect

- Sprint Planning
- Sprint Review
- Sprint Retrospective
- Daily Scrum
- Sprint

© 2026 Inspire | Confidential

Scrum Framework

3	3	5	5
• Product Owner: PO — maximizes product value • Scrum Master: SM — true leader who serves • Developers: create the usable Increment	• Product Backlog • Sprint Backlog • Product Increment	• Focus • Courage • Openness • Commitment • Respect	• Sprint Planning • Sprint Review • Sprint Retrospective • Daily Scrum • Sprint

© 2026 Inspire | Confidential

Scrum Roles



PRODUCT OWNER

SCRUM MASTER

DEVELOPERS

© 2026 Inspire | Confidential

Product Owner



PRODUCT OWNER


Per the Scrum Guide: the PO is accountable for maximizing the value of the product resulting from the work of the Scrum Team.
Also accountable for effective Product Backlog management.

Traits

- Domain expertise
- Communication
- Decision-making
- Ownership



Pitfalls



© 2026 Inspire | Confidential

Communication bridge

The PO is the communicator between the Scrum Team and external users.




SCRUM TEAM

Facing the Scrum Team, the PO represents the business and users in stating needs



PRODUCT OWNER




Business, users, leaders, etc.

Facing the business and users, the PO represents and speaks for the Scrum Team

© 2026 Inspire | Confidential

Work pace

The PO’s cadence is not identical to the team’s: during Sprint N, the PO prepares stories for Sprint N+1.

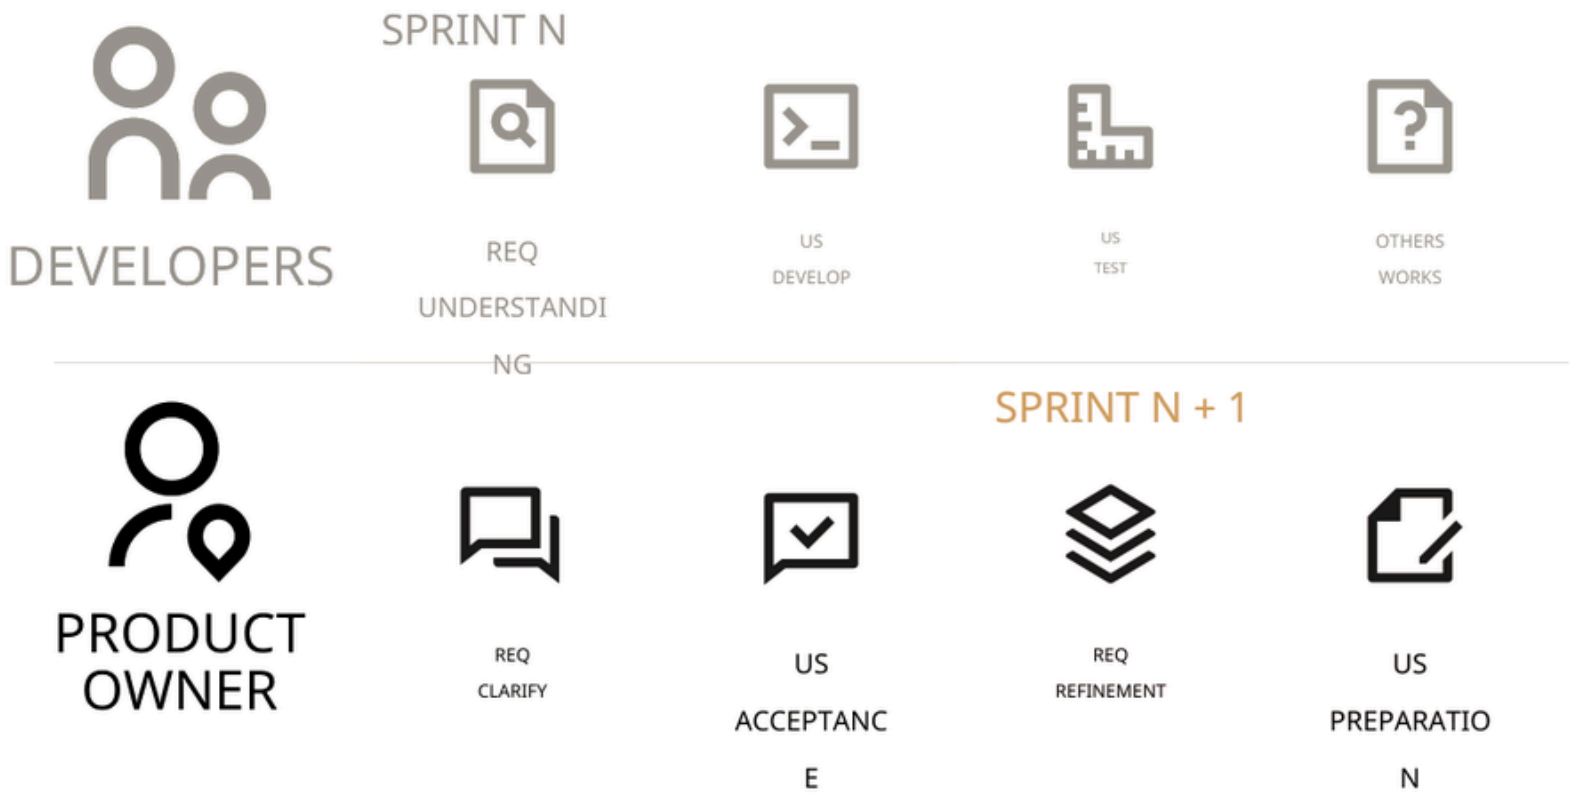

© 2026 Inspire | Confidential

Scrum Master · Leader Who Serves



Per the Scrum Guide: the Scrum Master is accountable for establishing Scrum as defined in the Guide, and for the Scrum Team's effectiveness.

Traits

- Patient
- Asks questions
- Protects the team
- Fair & transparent

Pitfalls


Beacon


Shepherd


Bulldozer


Overdoing


Over-control


Inactive

© 2026 Inspire | Confidential

Self-managing Scrum Team



DEVELOPERS

Developers are the people in the Scrum Team committed to creating any aspect of a usable Increment each Sprint. Structured and empowered by the organization, they manage their own work.

A Scrum Team shares one goal, is highly self-managing, and relentlessly improves

Focus



Goal



Self-mgmt



Collab

Pitfalls



No shared goal



Command & control



Relay-style work

© 2026 Inspire | Confidential



© 2026 Inspire | Confidential

Interpreting the Scrum Team

Which type is a Scrum Team?





© 2026 Inspire | Confidential

Self-managing team

COMMAND & CONTROL	SELF-ORGANIZING
Team members are assigned individual contributors	Team members are active, cross-skilled participants
Passively wait for instructions to assign work	Jointly plan and assign work together
Mostly solo work, little collaboration	Collaboration throughout the work
Docs and email as primary communication	Face-to-face is the primary communication
Finish personal tasks only — ignore team goals	Focus on team goals; shared accountability
Narrow skills; low motivation to learn	Broader skills; learn proactively for the role

© 2026 Inspire | Confidential

Scrum Framework



- Product Owner: PO — maximizes product value
- Scrum Master: SM — true leader who serves
- Developers: create the usable Increment


- Product Backlog
- Sprint Backlog
- Product Increment

- Focus
- Courage
- Openness
- Commitment
- Respect

- Sprint Planning
- Sprint Review
- Sprint Retrospective
- Daily Scrum
- Sprint

© 2026 Inspire | Confidential

Scrum Artifacts

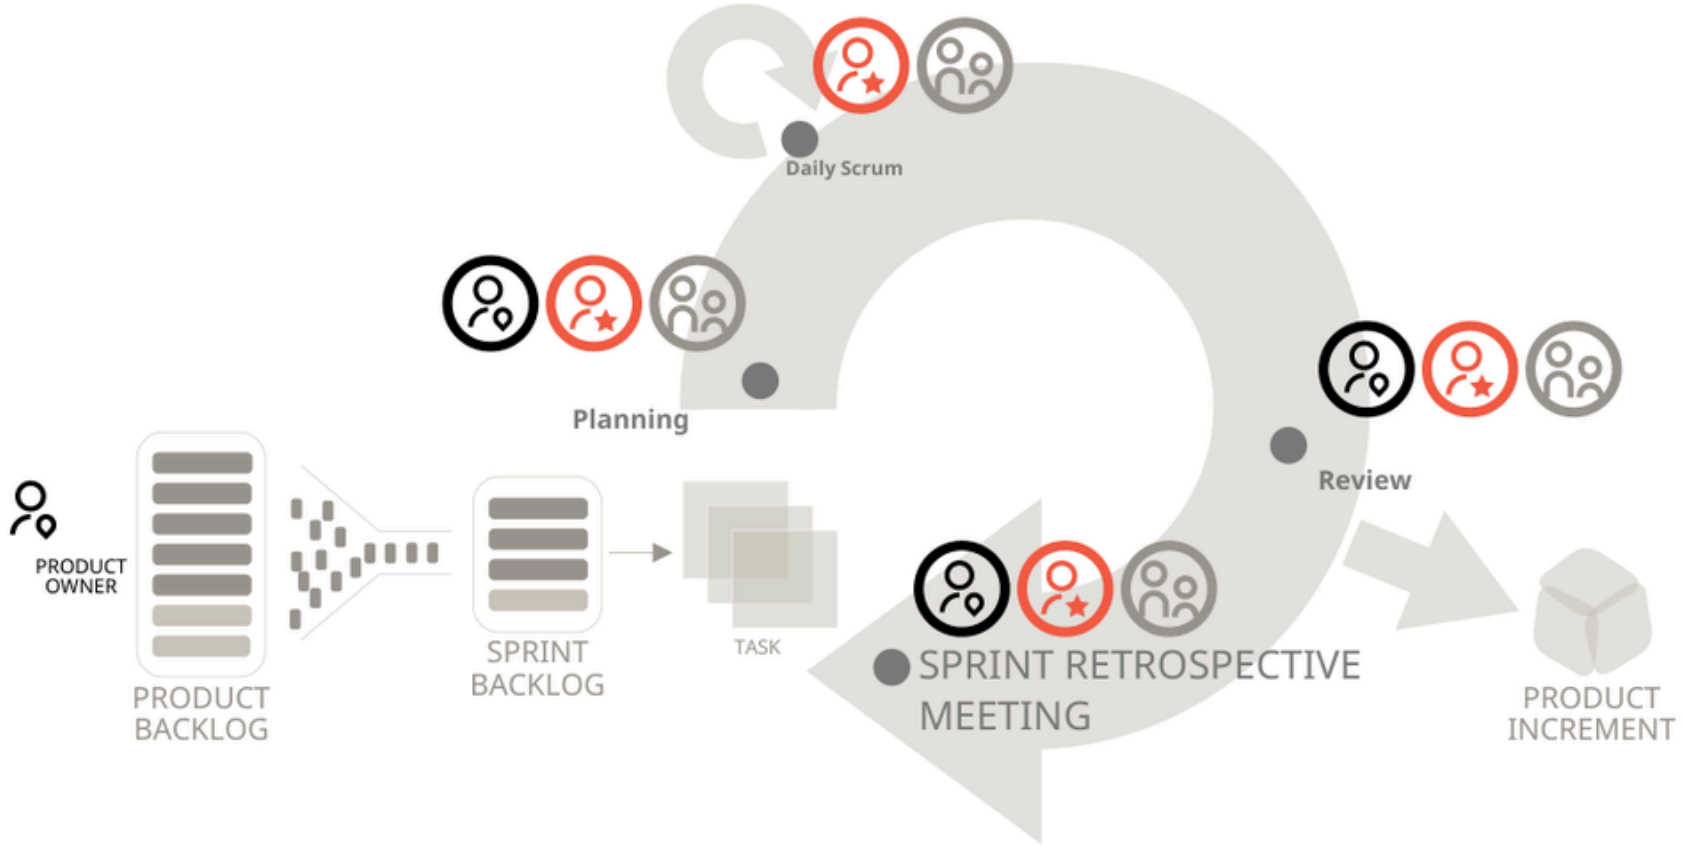


© 2026 Inspire | Confidential

Scrum Artifacts




© 2026 Inspire | Confidential

Product Backlog

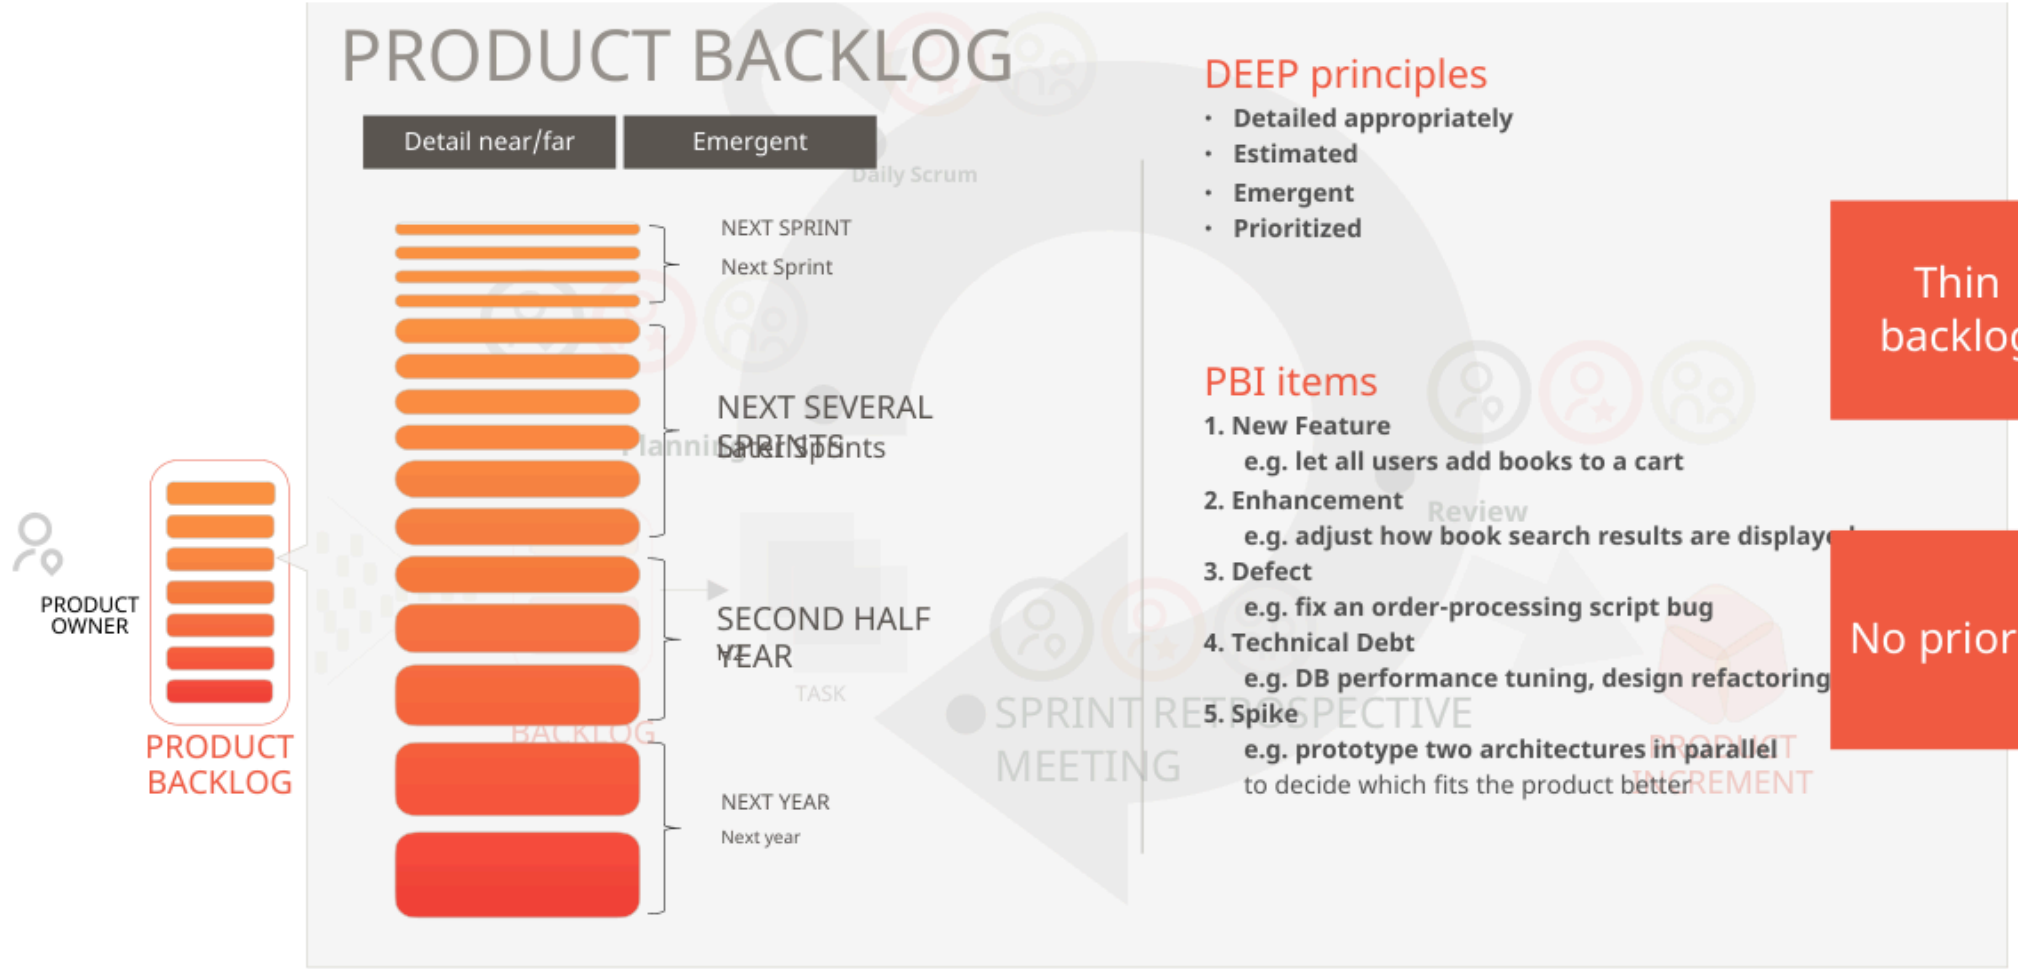


© 2026 Inspire | Confidential

Sprint Backlog

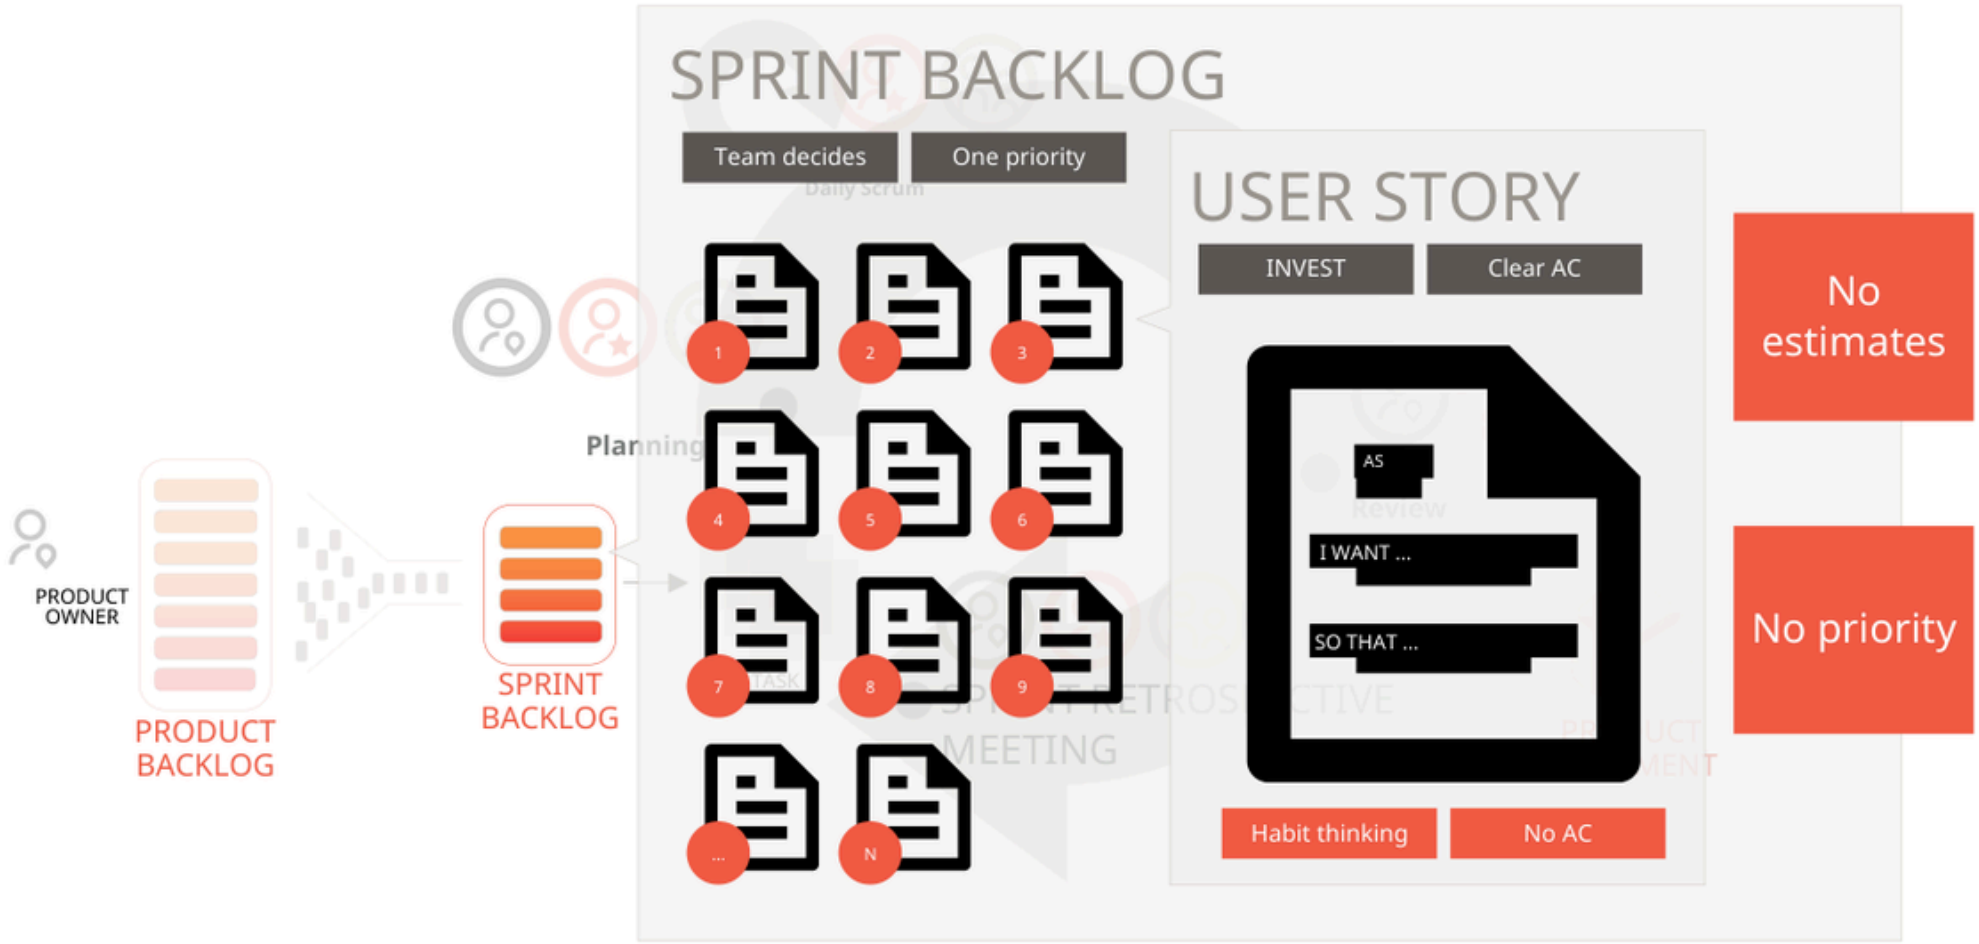

© 2026 Inspire | Confidential

Releasable Increment

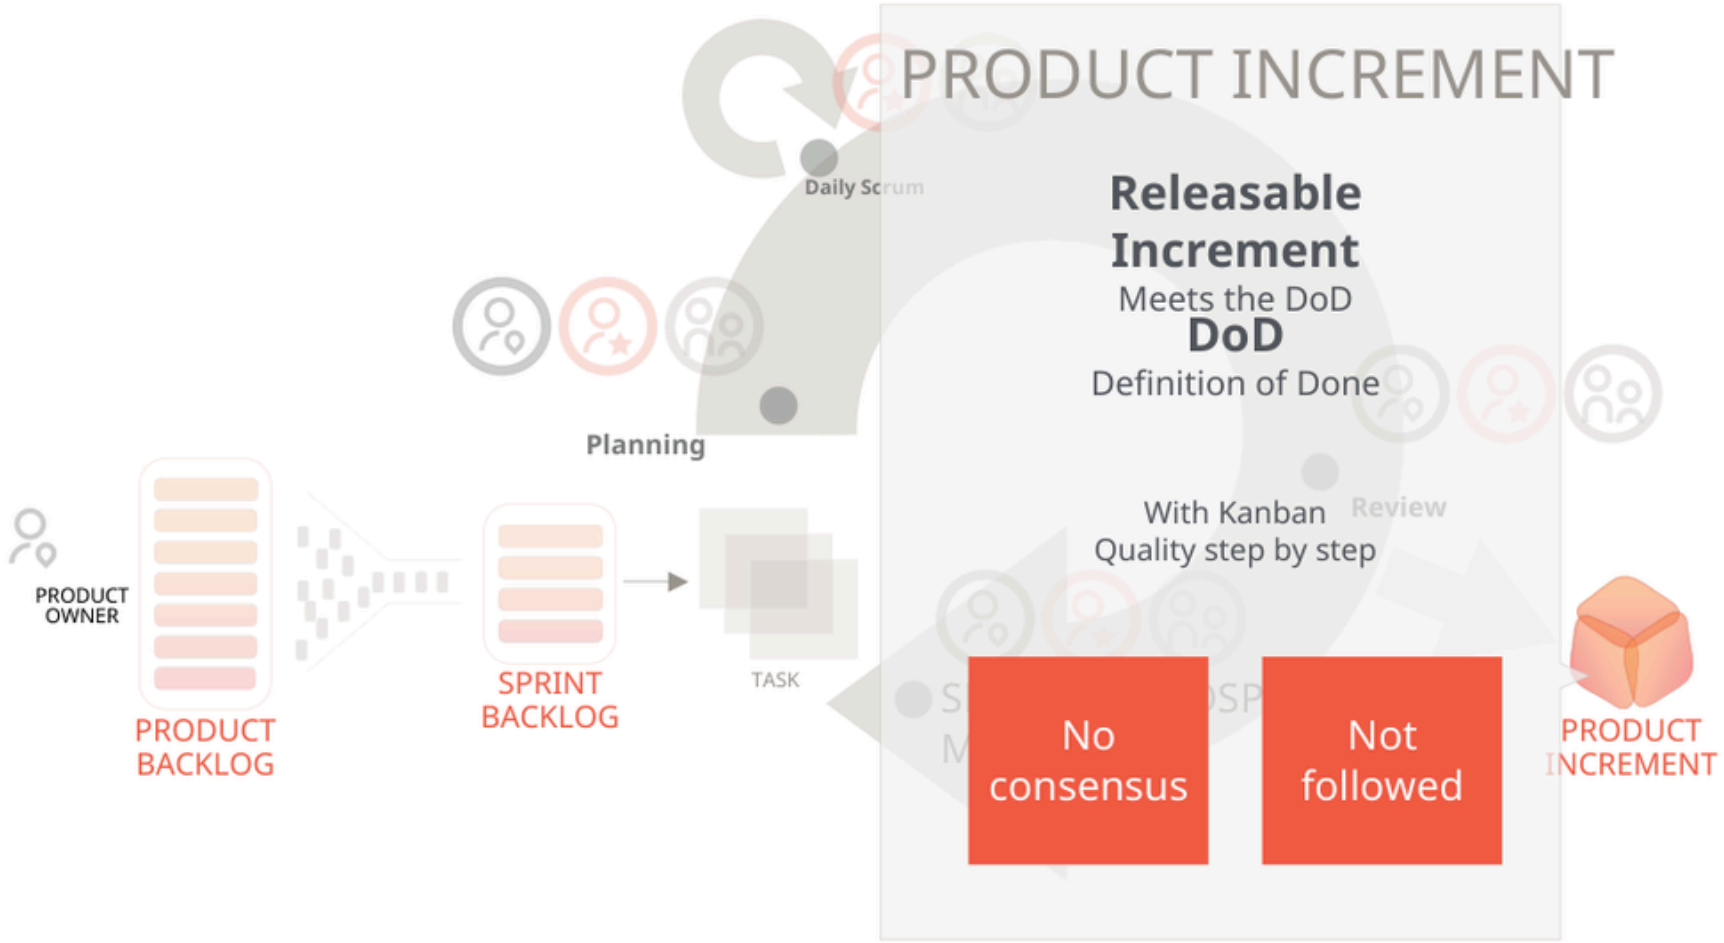

© 2026 Inspire | Confidential

Define DoD

User Story Done

- Story priority agreed with the business
- UI/UX design confirmed by the business
- UI/UX design confirmed by the team
- Story & code self-tested; meets AC
- Unit tests complete
- Daily code walkthrough done
- Daily build compiles with no errors
- Test cases 100% pass

PO owns

Sprint Done

- Integration tests 100% pass
- Regression tests 100% pass
- Business acceptance passed

Release Done

- Integrated release systems pass tests
- Security & performance pass tests
- All agreed defects verified fixed



© 2026 Inspire | Confidential

Scrum Framework



3 Roles

- Product Owner: PO — maximizes product value
- Scrum Master: SM — true leader who serves
- Developers: create the usable Increment



3 Artifacts

- Product Backlog
- Sprint Backlog
- Product Increment



5 Values

- Focus
- Courage
- Openness
- Commitment
- Respect




5 Events

- Sprint Planning
- Sprint Review
- Sprint Retrospective
- Daily Scrum
- Sprint

© 2026 Inspire | Confidential

Scrum Values

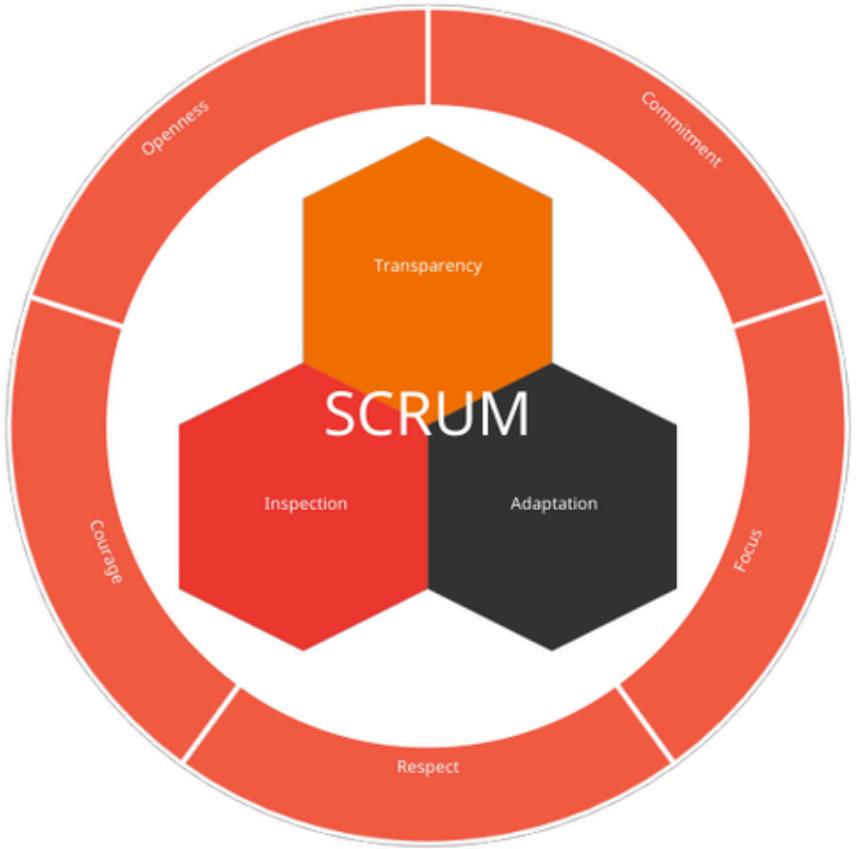

3 Pillars

- Transparency
- Inspection
- Adaptation

5 Values

- Openness
- Commitment
- Focus
- Respect
- Courage

© 2026 Inspire | Confidential

BREAK

Lunch



© 2026 Inspire | Confidential

INSPIRE AI

LECTURE

Scrum Essentials and Timeline Detail · Part 2

Empiricism and the project rhythm · Parts 1–2



© 2026 Inspire | Confidential

Scrum Framework



3 Roles

- Product Owner: PO — maximizes product value
- Scrum Master: SM — true leader who serves
- Developers: create the usable Increment



3 Artifacts

- Product Backlog
- Sprint Backlog
- Product Increment



5 Values

- Focus
- Courage
- Openness
- Commitment
- Respect



5 Events

- Sprint Planning
- Sprint Review
- Sprint Retrospective
- Daily Scrum
- Sprint


© 2026 Inspire | Confidential

Scrum Events



© 2026 Inspire | Confidential

Scrum Events

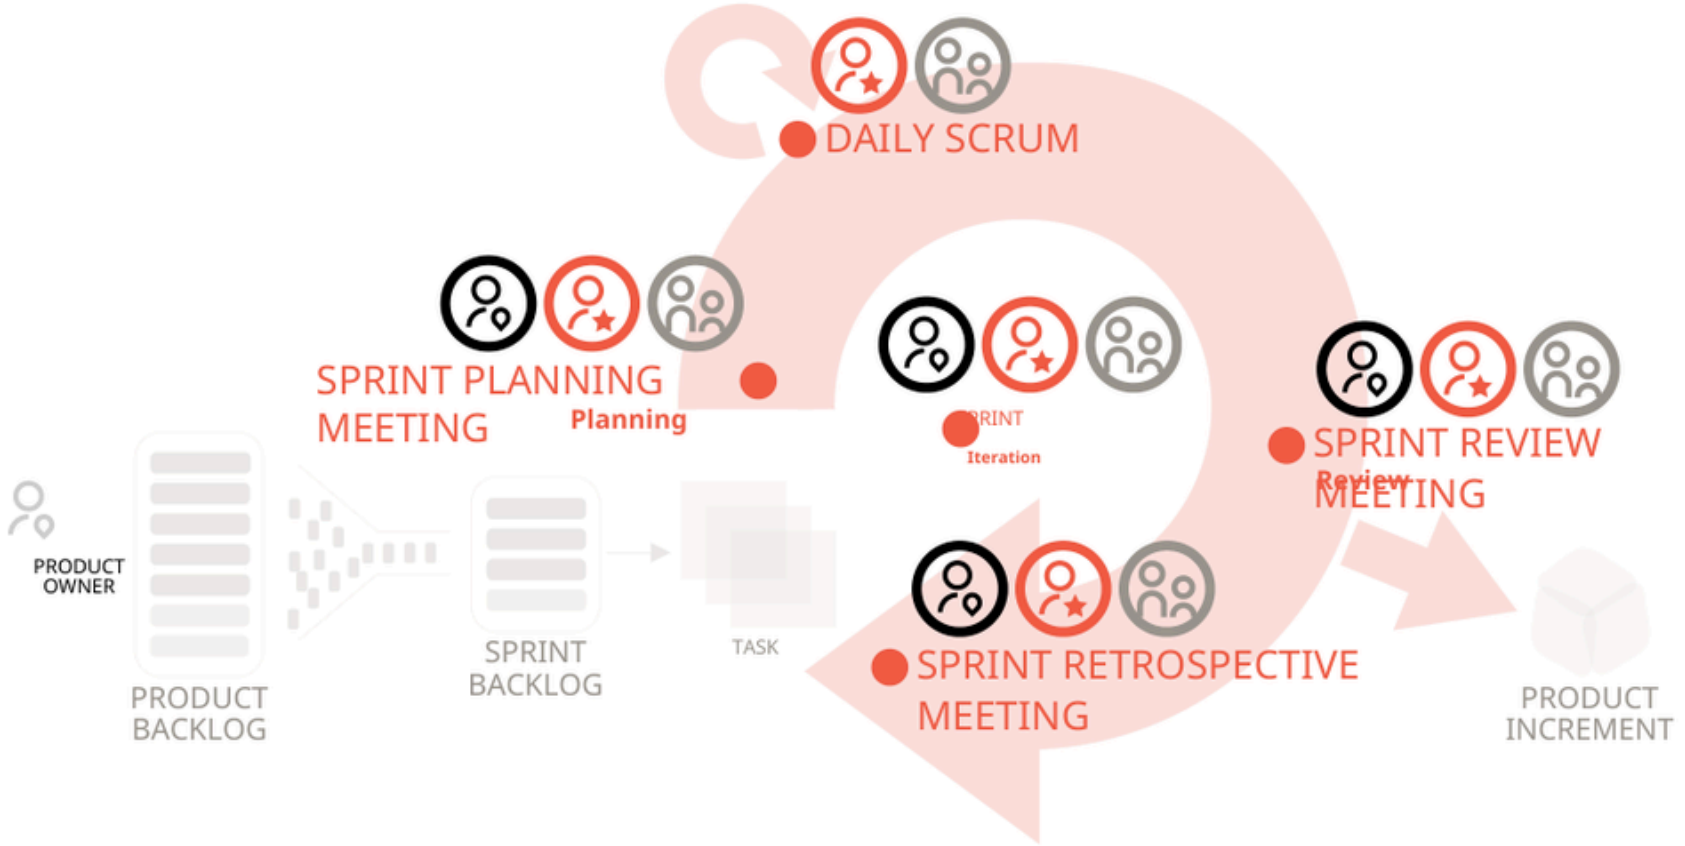

© 2026 Inspire | Confidential

BACKLOG REFINEMENT

Purpose

Common pitfalls:
Vague requirements, not asking, no prep before the event

The Product Owner walks the Scrum Team through candidate Product Backlog items for the next Sprint, identifies and answers questions, so Sprint Planning is more effective

Info

Wednesday before each Sprint starts	Whole team attends; PO facilitates	2–4 hours	
Defined user stories and related info, plus a prioritized Product Backlog			
Updated Product Backlog and stories, estimates (e.g. story points), open questions			

1. The Product Owner shares recent Backlog changes — new needs, priority shifts (including tech stories, defects, Spikes)
2. Walk through stories from highest priority down; the team makes initial estimates
3. During Product Backlog refinement, items may be adjusted — re-ordered and split
4. During refinement, capture questions that cannot be answered immediately (requirements and technical)
5. During refinement, deliberately identify and record delivery risks

© 2026 Inspire | Confidential

SPRINT PLANNING

Purpose

The Product Owner and Scrum Team agree on the committed delivery scope for a Sprint

Common pitfalls:
Unclear Sprint Goal, weak detail & risk analysis

Info

When: End of last Sprint or start of this Sprint	Who: Whole team attends; SM facilitates	Duration: 1–4 hours
Input: Product Backlog (at least Stories the PO expects this Sprint, with priority), AC, DoD, prototypes		
Output: Sprint Backlog (with estimates), Sprint Goal, owner for each story		

1. Present the highest-priority Stories and confirm with the PO whether adjustments are needed
2. The team confirms story points it can commit to, considering velocity, leave, and other support work
3. Together, select enough Stories from high to low priority for a commit-able Sprint plan (able to meet DoD within the Sprint)
4. Optionally pick a few extra Stories (2–3) as Sprint stretch goals
5. Reconfirm with the PO the in-Sprint priority order and clarify the Sprint Goal
6. Team members pull Stories they own from the Sprint plan and estimate effort
7. After Planning, the SM helps the team update the board with the new plan

© 2026 Inspire | Confidential

DAILY SCRUM

Common pitfalls:
Status reporting, disengaged, problem-solving in the meeting

Purpose

Team members sync on progress and issues to improve collaboration

Info

- Same time every day
- Whole team attends; SM facilitates
- 10–15 minutes
- Each person's progress and impediments
- Updated board and recorded impediments

1. First, check progress on existing risks and impediments on the board
2. Each member, against their board items, answers: What did I progress yesterday? What will I do today? What is blocking me?
3. While answering, each person updates their board items
4. For flagged items (risk, dependency, or delay), update status with extra focus
5. The Scrum Master facilitates impediments and owners (coordinate resolution after the meeting)

© 2026 Inspire | Confidential

SPRINT REVIEW

Purpose

Common pitfalls:
No prep; demo-only Review; hidden issues; no feedback

The team regularly inspects progress, discusses risks, and adapts the plan; and demos completed Stories to the Product Owner to gather feedback

Info

	Weekly, or at the end of each Sprint		SM facilitates; PO, Team, and invited stakeholders
	Sprint progress, demoable Story list, demo environment		1 hour
	Feedback on the demo; adapted Sprint plan		

1. Beforehand, the PO shares demo expectations (Story list or key paths)
2. The team prepares demo data/environment and checks the room 10 minutes early
3. Team members demo completed Stories to the PO and stakeholders; capture feedback
4. Summarize Sprint progress, surface issues and risks, discuss how to resolve
5. If planned Stories cannot be delivered, negotiate Sprint plan changes with the PO

© 2026 Inspire | Confidential

SPRINT RETROSPECTIVE

Purpose

Inspect people, relationships, process, and tools from the last Sprint
Identify what went well, what to improve, and an improvement plan

Common pitfalls:
Blame; no improvement/tracking; vague & superficial


Info

Last day of each Sprint	SM facilitates; PO and Team	1–2 hours
Metrics collected during the Sprint; team issues and pain points		
What went well / poorly; improvement Actions for top-priority issues		

1. Beforehand, the Scrum Master analyzes Sprint metrics
2. Ensure psychological safety; declare ground rules (e.g. no personal attacks)
3. SM shares metric analysis; serious issues become retrospective topics
4. As a team, summarize goods/bads; use fishbone, affinity, etc. to converge on next-Sprint improvements
5. Propose Actions for each issue — concrete, with due date and owner

© 2026 Inspire | Confidential

Scrum Events

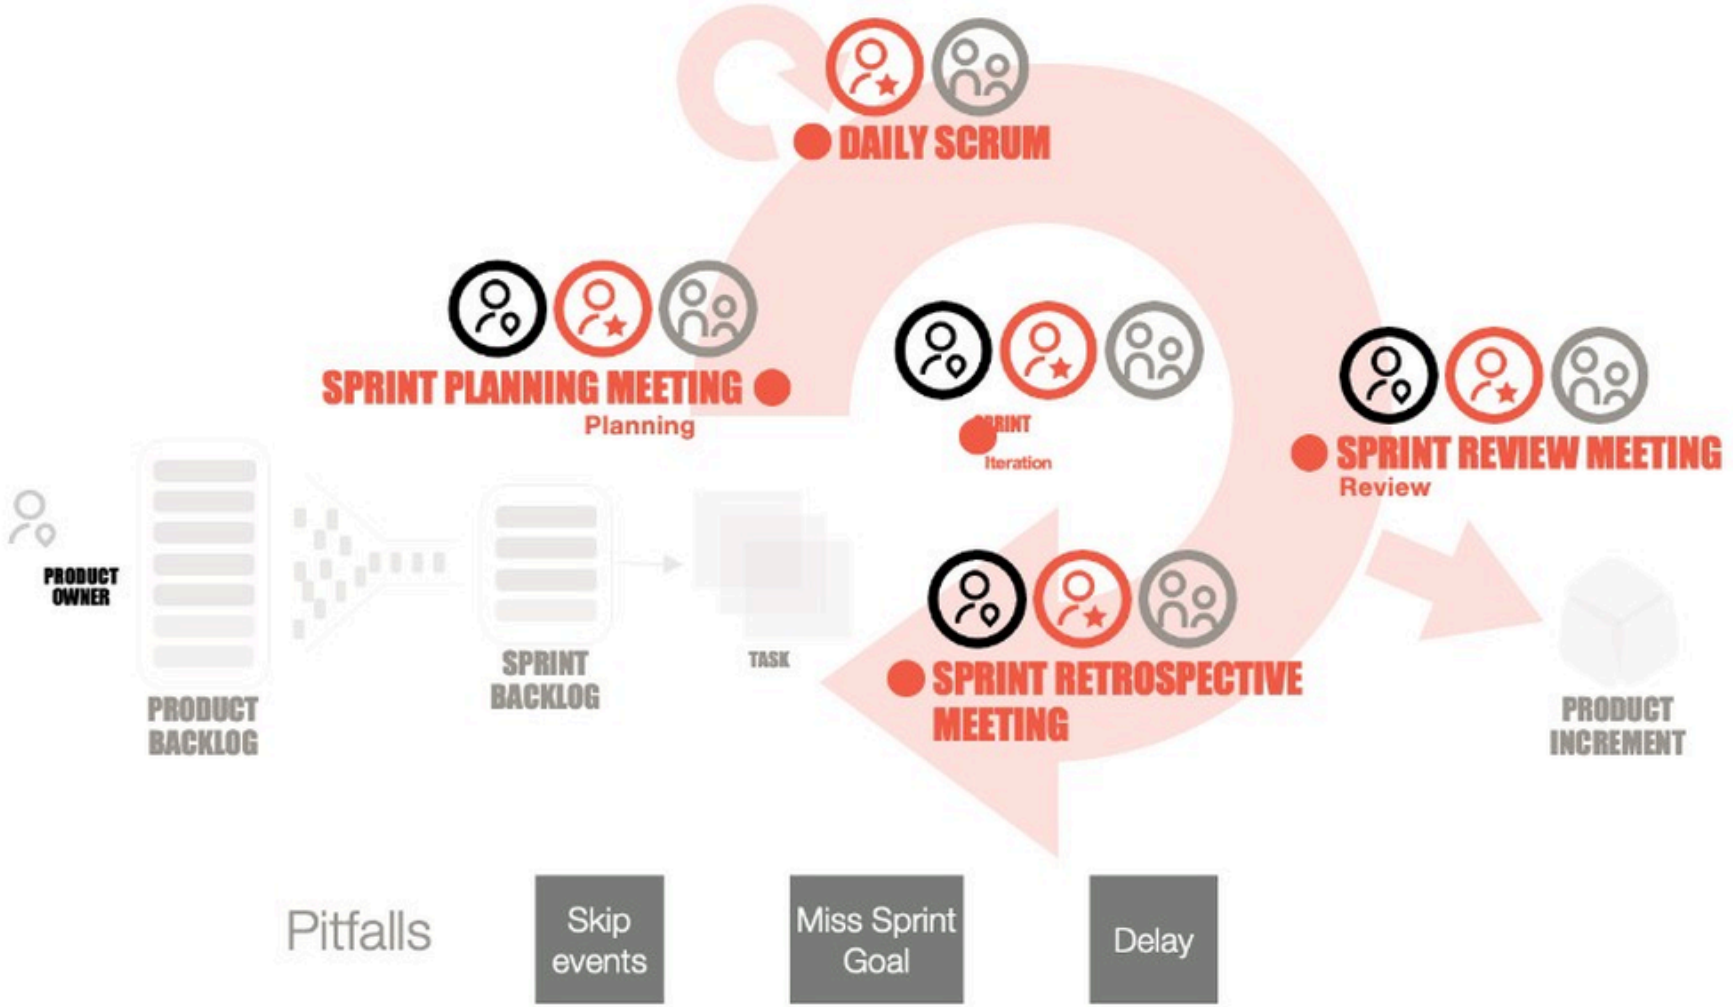

© 2026 Inspire | Confidential

Sprint Calendar



Planning

Whole Scrum Team plans: select this Sprint's Product Backlog items and set the Sprint Goal

- Sprint Day 1
- SM、PO、TEAM
- 2 ~ 4 HOUR

Daily Scrum

At the Daily Scrum, inspect progress toward the Sprint Goal and identify impediments and risks

- Every Sprint day (except Day 1)
- SM, Team, PO (optional)
- 10~15 MIN

Refinement

PO walks the team through next-Sprint Product Backlog items, answers questions; Developers estimate

- Week 2, Day 3
- SM、PO、TEAM
- 2 ~ 4 HOUR

Review

Inspect the Increment with the PO and stakeholders; gather feedback

- Week 2, Day 4
- SM, PO, Team, stakeholders
- 1 ~ 2 HOUR

Whole-team Sprint Retrospective: what went well / not, and concrete Actions

- Last day of the Sprint
- SM、PO、TEAM
- 1~2 HOUR

© 2026 Inspire | Confidential

Iteration-day rhythm (from Day 16)

- 08:40 Standup
- 09:00 Regular Showcase to PO（G2）
- 10:00 IPM if needed（G1）
- Build / kickoff / desk check through the day
- 16:00 Code Review in team — actions same day
- 17:00 Retro on Tuesday & Thursday

© 2026 Inspire | Confidential

BREAK

Take a short break



© 2026 Inspire | Confidential

INSPIRE AI

LECTURE

Iteration 0 · Iteration Planning Meeting

Plan the runway



© 2026 Inspire | Confidential

Sprint Planning Meeting

- Done in last sprint
- Introduce current sprint stories and estimate
- Finalize sprint scope



迭代20-信用债盯市 66 问题 活跃

35.5 17 54.5

+3 2023-05-05 16:02:09 • 2023-05-12 16:02:00 查看链接的页面

AP-1636	【利率债】国债（0.5.50]年非发行期限，统计对应的【样本区间】内【活跃债券】的经纪成交笔数	0407发布版本V4.6.0.0	利率债编制场景 1
AP-937	【利率债】曲线编制-编制内页（自动编制-活跃券范围）	0407发布版本V4.6.0.0	利率债编制场景 2
AP-941	【利率债】曲线编制（自动编制-批量计算）	0407发布版本V4.6.0.0	利率债编制场景 2
AP-938	【利率债】曲线编制-编制内页（自动编制-国债曲线）	0407发布版本V4.6.0.0	利率债编制场景 3
AP-939	【利率债】曲线编制-编制内页（自动编制-政金债曲线）	0407发布版本V4.6.0.0	利率债编制场景 3
AP-940	【利率债】曲线编制-编制内页（自动编制-财政部地方政府债）	0407发布版本V4.6.0.0	利率债编制场景 3
AP-1250	【综合屏】行情、舆情、信用分析前端界面优化		综合屏功能
AP-1756	【信用债】估值编制-盯市参数配置（信用债+同业存单+交易所+操作按钮）	0512发布版本V4.8.0.0	信用债编制场景 4
AP-1749	【信用债】行情数据-整合成交页面（前端映射）	0421发布版本V4.7.0.0	信用债编制场景 2
AP-1752	【信用债】估值编制-估值列表-盯市tab（列表+筛选）前端	0421发布版本V4.7.0.0	信用债编制场景 2
AP-1755	【信用债】估值编制-白名单维护（新增、查询、编辑）	0512发布版本V4.8.0.0	信用债编制场景 4
AP-1350	【境外债】自动编制收益率反算点差推荐方向问题		境外债编制场景 2
AP-1759	【信用债】估值编制-自动计算逻辑-整体流程框架		信用债编制场景 15
AP-1760	【信用债】估值编制-自动计算逻辑-剔除白名单数据		信用债编制场景 2
AP-1761	【信用债】估值编制-自动计算逻辑-一般信用债可靠价格加工		信用债编制场景 3



© 2026 Inspire | Confidential

INSPIRE AI

PRACTICE

Iteration 0 · IPM Practice

Select stories and make risks visible



© 2026 Inspire | Confidential

Plan the runway — not the whole product

01 **Iteration goal**
One sentence for I1 outcome.

02 **Pull ready stories**
Only AC-ready cards.

03 **Capacity & risks**
Who · blockers · deps.

04 **Demo path**
How you will show it Friday-week.

© 2026 Inspire | Confidential

PRACTICE


Iteration 0 · Kanban Setup

Visualize flow on a shared board



© 2026 Inspire | Confidential

KANBAN SETUP



© 2026 Inspire | Confidential

INSPIRE AI

COACHING

Iteration 0 · P0 Engineering Harness and Environment Setup

Repo, CI path, walking skeleton



© 2026 Inspire | Confidential

What must be green before Monday

01 **Repo ready**
Shared repo · branch rules · access.

02 **CI path**
Build · test · quality gate feedback.

03 **Walking skeleton**
Minimal running harness.

04 **Story ready**
I1 stories with AC on the board.

© 2026 Inspire | Confidential

CI / CD and environments

-

Setup today

- Repo + CI pipeline path
- Dev / UAT path clear
- Auto-trigger agreed
- Who owns the red build

Board columns to add

- Standard flow columns
- Code Review Action
- Code Review Action Done
- Same-day CR discipline

© 2026 Inspire | Confidential

PRACTICE

Project Readiness Gate

Readiness check tonight, then the real iteration



© 2026 Inspire | Confidential

Let’s start the real iteration

Follow the daily rhythm. Keep actions same day.

AI may help — you still own acceptance.

© 2026 Inspire | Confidential
